


Kronologija dogodkov 2008 – 2013

	Rotnik / Brežar		Tot / Žgajner		Rosec / Rosec	Dermol / Črep
	NIP 3	NIP 4	NIP 5	Trenutno stanje		
Vrednost investicije	1.189.117,100 €	1.302.747,000 €	1.302.492,300 €	1.440.468,733 €		
Vrednost opreme	963.950,200 €	1.063.420,700 €	1.126.738,500 €	1.194.140,33		
Gradbeno delo	83.697,300 €	75.969,300 €	67.589,700 €	77.401,475 €		
Stroški financiranja	131.058,900 €	128.550,200 €	82.096,200 €	133.410,870 €		

Dodaten strošek na GTD	Vpliv na terminski plan	PAC	27.6.08	1.11.09	19.10.09	2.12.09	21.1.11	1.8.12	15.9.11	23.12.11	4.6.12	1.9.12	30.10.12	21.12.12	4.2.13	4.2.13	4.2.13
/	/	/	/	/	/	/	-1.035.000	4.500.000 6.200.000	2.295.342 4.700.000	1.722.108 1.596.470	1.750.000	/	min 7.300.000	/	/	/	14.950.000 (posledica dodatka B) -134.000 7.800
								+105 dni	+31 dni	+26 dni +30 dni	+14 dni		min +51 dni				+154 dni (posledica dodatka B)
			November 2014	November 2014	November 2014	November 2014	November 2014	15.3.2015	17.4.2015	12.6.2015	26.6.2015	26.6.2015	15.8.2015	15.8.2015	15.8.2015	15.8.2015	27.11.2015

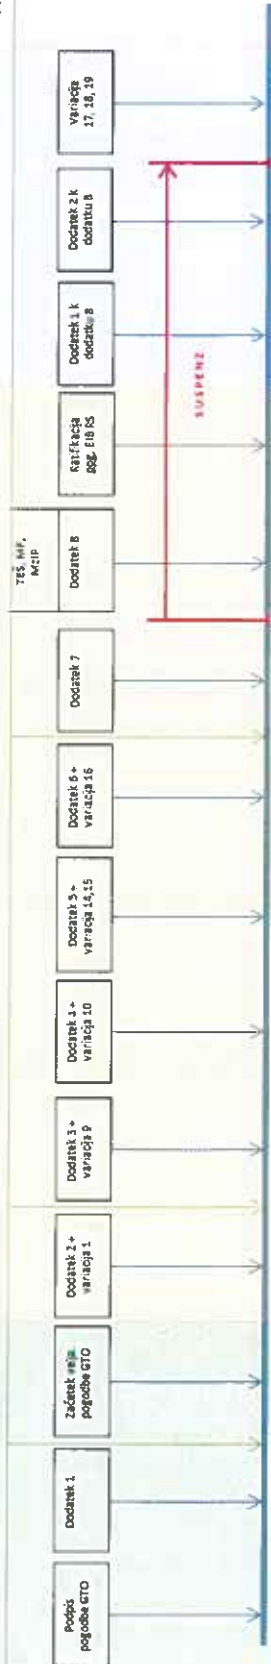

TERMOELEKTRARNA ŠOŠTANJ d.o.o.
